

FLOWPETROL S.A.		BHP JOB	
LO16-7 OFFICIAL NUMBER	LO16-7 SAVIA PERU NUMBER	LOBITOS - OFFSHORE AREA	
		BLT GAS LIFT CURRENT INSTALLATION TYPE	FLOWING & STATIC GRADIENT BHP TEST
LO16-7 WELL FLUID LEVEL, 7245' BK-1, 7590' MEMORY, 7598' STD VALVE, 7603' Sand Top 7840' TD : 8074' 7016' B.S. 8032'		REMARKS: Oil Production: 14 BOPD X 2 BWPD Cycle: 60' X 6' BK1 - Depth: 7590' Std. Valve Depth: 7603' <u>February 09th, 2011</u> 8:25 Arrived on location, LO16 platform 8:45 Safety meeting with all crew involved. 8:55 RIG Up BOP & Lubricator over LO16-7 well. 10:10 RIH 1 1/2" dead weight up to 7603' Standing Valve depth. 10:35 Activate memory gauges 2760 w/ battery PPS 8060C 10:45 RIH memory gauges with steps to find flowing fluid level. 0' - 7145' - 7195' - 7245' - 7295' - 7345' - 7395' - 7445' - 7495' - 7515' - 7535' - 7555' - 7575' - 7595'. 11:20 Hang up Memory Gauges at 7598', Record 3hr at flowing condition. Production total: 2.3 bls in 3hs. (3cycles of 60 x 6' aprox 0.8 Bls/ cycle) THP (2 3/8" tbg) = 25 psia - 70 psia. THP (1 1/4" tbg) = 450 psia - 880 psia. 14:25 Cut off Gas Lift Injection and production valve, continue logging for 2 hrs. THP (2 3/8" tbg) = 25 psia. THP (1 1/4" tbg) = 440 psia. 16:25 POOH Memory Gauges with steps as follow: 7595' - 7545' - 7495' - 7445' - 7395' - 7345' - 7295' - 7245' - 7195' - 7145' - 7095' - 7045' - 6945' - 6845' - 6745' - 6645' - 0'. 17:10 Memory gauges on Surface. 17:18 Desactivate Memory. 18:00 RIG Down. MEMORY GAUGES PROGRAMM 1.- 30 SEG/SAMPLES 6.5 HRS 780 SAMPLES MAX. CAPACITY: 500000 SAMPLES	

SUMMARY OF BHP RESULTS : LO16-7

Date of Test	February 09th, 2011
Formation	Basal Salina < 8032' - 7016' >
Gauges Serial Number	2760
Gauges Depth	7595 MD ft
	7076 VD ft

Memory Gauges @ 7598', Record at flowing Condition for 3 hr

THP 2 3/8	25-70 psia
THP 1 1/4	450 - 880 psia
Pwf min	114 psia
Temperature min:	117 ° F
Pwf max	145 psia
Temperature max:	118 ° F
Oil production:	14 BOPD
Water production:	2 BWPD
Cycle injection:	60' X 6'
Production during the test:	2.3 Bls
Production per cycle:	0,8 Bls/Cycle
Oil level:	7245
Oil Gradient:	0,252
Flowing Gradient:	0,020 psi/ft

Cut off Gas lift injection and Production valve, log for 2 hr

THP 2 3/8	25 psia
THP 1 1/4	440 psia
P St initial	144 psia
Temperature:	118 ° F
P St final	148 psia
Temperature:	118 ° F
Oil level:	7445 ft
Oil Gradient:	0,353 psi/ft
Static Gradient:	0,021 psi/ft


Fluid Level at Flowing Condition While RIH MG's			
---	--	--	--

MD (ft)	TVD (ft)	PRESSURE (psi)	GRADIENT (psi/ft)
0	0	16	-
7145	6680	41	0,004
7195	6723	41	0,047
7245	6767	43	0,341
7295	6811	58	0,341
7345	6855	73	0,159
7395	6899	80	0,341
7445	6943	95	0,114
7495	6987	100	0,159
7515	7005	107	0,278
7535	7023	112	0,333
7555	7040	118	0,118
7575	7058	120	0,056
7595	7076	121	0,056

Fluid Level & Gradients			
-------------------------	--	--	--

FLUID TYPE	MD (ft)	TVD (ft)	GRADIENT (psi/ft)
GAS	0	0	0,0037
OIL	7245	6767	0,2524
GAUGES	7595	7076	0,0171

Flowing Pressure, LO16- 7 Well

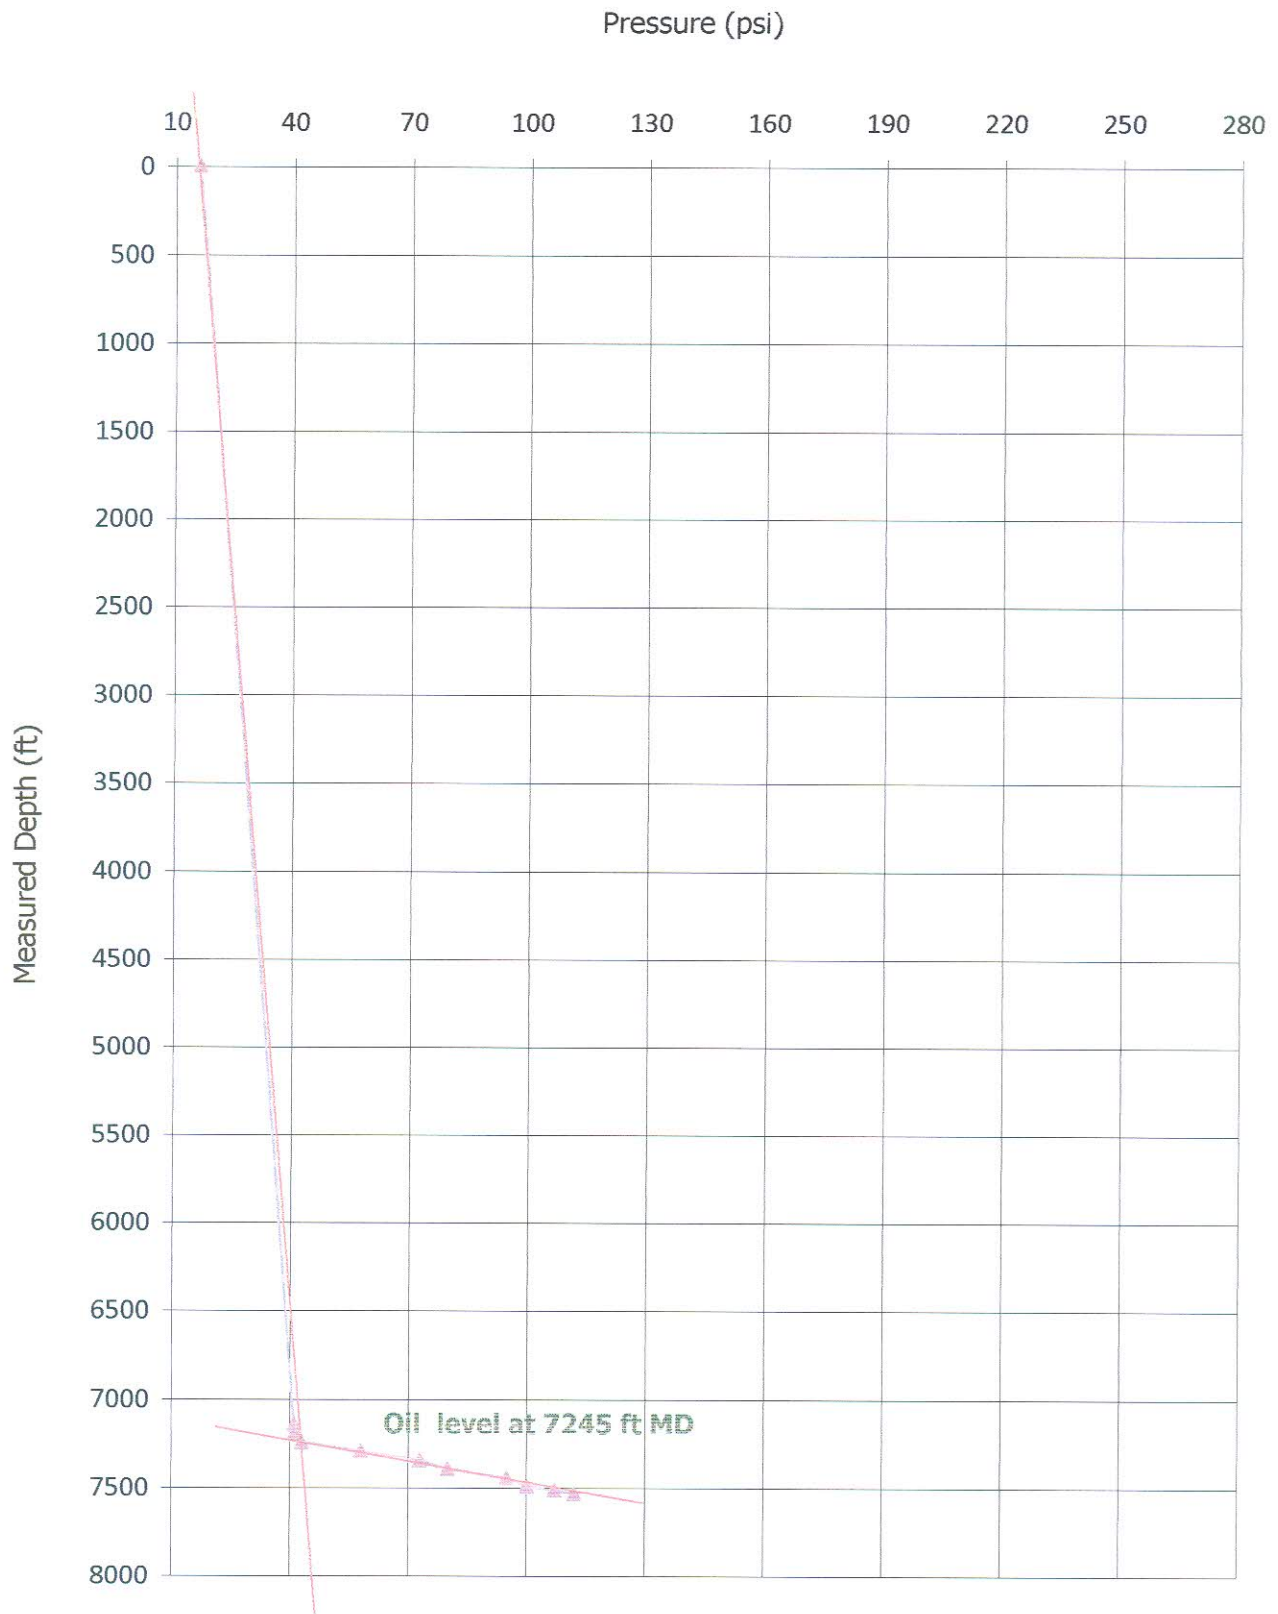


Fluid Level at Static Condition While POOH MG's			
---	--	--	--

MD (ft)	TVD (ft)	PRESSURE (psi)	GRADIENT (psi/ft)
0	0	16	-
6645	6325	41	0,0040
6745	6324	41	0,0000
6845	6414	41	0,0000
6945	6503	41	0,0000
7045	6592	41	0,0000
7095	6636	41	0,0000
7145	6680	41	0,0000
7195	6727	41	0,0000
7245	6767	41	0,0000
7295	6811	41	0,0000
7345	6855	52	0,2500
7395	6899	68	0,3636
7445	6943	83	0,3409
7495	6987	99	0,3636
7545	7032	115	0,3556
7595	7076	130	0,3409

Fluid Level & Gradients			
-------------------------	--	--	--


FLUID TYPE	MD (ft)	TVD (ft)	GRADIENT (psi/ft)
GAS	0	0	0,0037
OIL	7445	6943	0,3529
GAUGES	7595	7076	0,0184

Static Pressure, LO16 - 7 Well

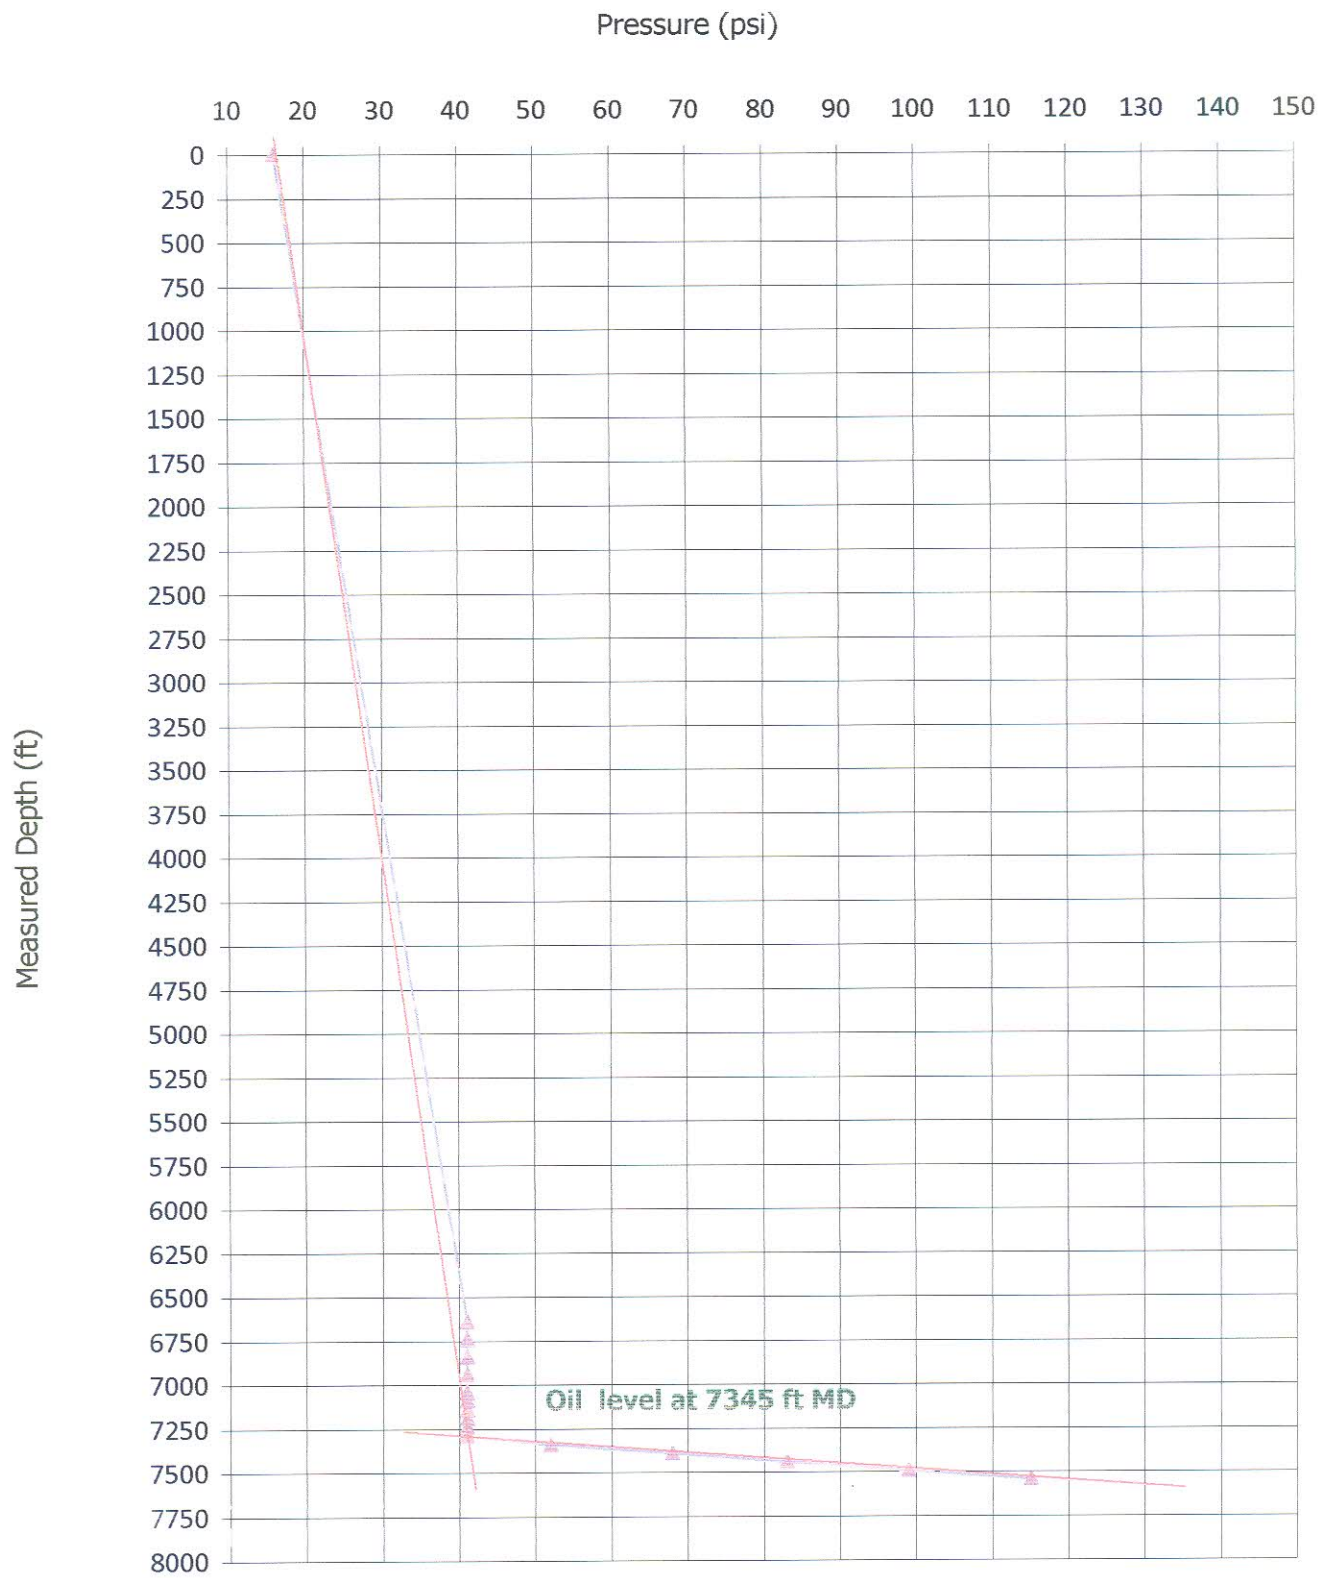

Flowing & Static Gradient BHP Test, LO16-7 Well.

Memory gauges at 7598 ft MD

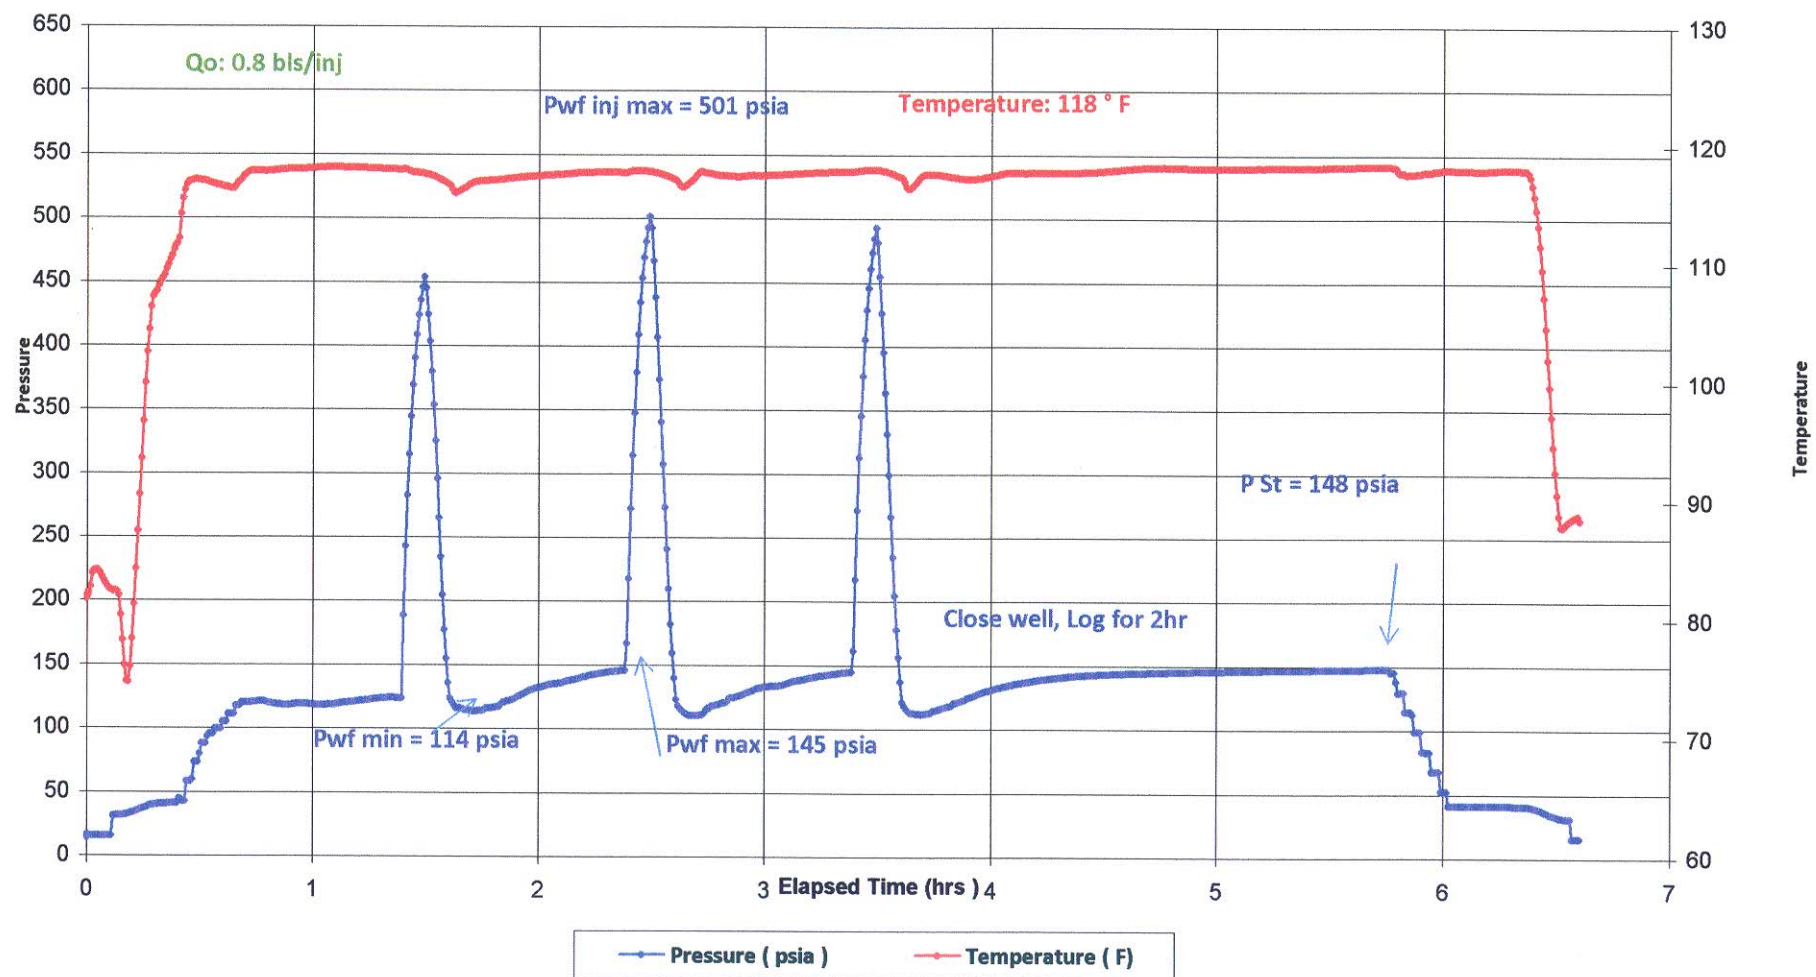

Well: LO16-7 Development Test
Memory Gauge: SN 2760 with Battery PPS 8060C
Time Elapsed Time Pressure Temperature
(Real - Time) (Hours) (Psia) (DegF)

09/02/2011 10:35	0,00028	16,26	81,684
09/02/2011 10:35	0,00056	16,237	81,817
09/02/2011 10:35	0,00083	16,205	81,85
09/02/2011 10:35	0,00111	16,146	81,896
09/02/2011 10:35	0,00139	16,088	81,906
09/02/2011 10:35	0,00167	16,027	81,911
09/02/2011 10:35	0,00194	15,988	81,931
09/02/2011 10:35	0,00222	15,968	81,933
09/02/2011 10:35	0,0025	15,963	81,944
09/02/2011 10:35	0,00278	14,806	81,982
09/02/2011 10:35	0,00306	14,3	82,002
09/02/2011 10:35	0,00333	15,057	82,007
09/02/2011 10:35	0,00361	15,096	82,007
09/02/2011 10:35	0,00389	15,01	82,021
09/02/2011 10:35	0,00417	15,024	82,017
09/02/2011 10:35	0,00444	15,905	82,013
09/02/2011 10:35	0,00472	15,673	82,046
09/02/2011 10:35	0,005	15,903	82,037
09/02/2011 10:35	0,00528	16,578	81,902
09/02/2011 10:35	0,00556	15,665	82,116
09/02/2011 10:35	0,00583	15,663	82,113
09/02/2011 10:35	0,00611	15,653	82,106
09/02/2011 10:35	0,00639	16,189	82,025
09/02/2011 10:35	0,00667	16,718	81,975
09/02/2011 10:35	0,00694	15,734	82,095
09/02/2011 10:35	0,00722	16,021	82,164
09/02/2011 10:35	0,0075	15,679	82,168
09/02/2011 10:35	0,00778	15,679	82,175
09/02/2011 10:35	0,00806	15,674	82,192
09/02/2011 10:35	0,00833	15,666	82,195
09/02/2011 10:35	0,00861	15,662	82,215
09/02/2011 10:35	0,00972	15,662	82,241
09/02/2011 10:36	0,01806	15,654	82,686
09/02/2011 10:36	0,02639	15,65	83,828
09/02/2011 10:37	0,03472	15,653	84,032
09/02/2011 10:37	0,04306	15,653	84,097
09/02/2011 10:38	0,05139	15,651	84,086
09/02/2011 10:38	0,05972	15,655	83,876
09/02/2011 10:39	0,06806	15,664	83,58
09/02/2011 10:39	0,07639	15,668	83,26
09/02/2011 10:40	0,08472	15,669	82,978
09/02/2011 10:40	0,09306	15,668	82,679
09/02/2011 10:41	0,10139	15,667	82,499
09/02/2011 10:41	0,10972	15,664	82,405
09/02/2011 10:42	0,11806	31,407	82,332
09/02/2011 10:42	0,12639	31,431	82,384
09/02/2011 10:43	0,13472	31,471	82,332
09/02/2011 10:43	0,14306	31,532	81,975
09/02/2011 10:44	0,15139	31,642	80,341
09/02/2011 10:44	0,15972	31,809	78,219
RIH MEMORY GAUGES WITH STEPS			
09/02/2011 10:45	0,16806	32,05	76,069
09/02/2011 10:45	0,17639	32,395	74,76
09/02/2011 10:46	0,18472	32,832	74,673
09/02/2011 10:46	0,19306	33,326	75,967
09/02/2011 10:47	0,20139	33,843	78,327
09/02/2011 10:47	0,20972	34,379	81,212
09/02/2011 10:48	0,21806	34,91	84,192
09/02/2011 10:48	0,22639	35,448	87,388
09/02/2011 10:49	0,23472	36,024	90,499
09/02/2011 10:49	0,24306	36,622	93,55
09/02/2011 10:50	0,25139	37,238	96,69
09/02/2011 10:50	0,25972	37,865	99,924
09/02/2011 10:51	0,26806	38,455	102,552
09/02/2011 10:51	0,27639	39,014	104,402

Well: LO16-7 Development Test
Memory Gauge: SN 2760 with Battery PPS 8060C
Time Elapsed Time Pressure Temperature
(Real - Time) (Hours) (Psia) (DegF)

09/02/2011 10:52	0,28472	39,516	106,304
09/02/2011 10:52	0,29306	39,919	107,168
09/02/2011 10:53	0,30139	40,228	107,466
09/02/2011 10:53	0,30972	40,468	107,684
09/02/2011 10:54	0,31806	40,618	108,129
09/02/2011 10:54	0,32639	40,734	108,513
09/02/2011 10:55	0,33472	40,813	108,785
09/02/2011 10:55	0,34306	40,886	109,035
Step at 7145'			
09/02/2011 10:56	0,35139	40,962	109,501
09/02/2011 10:56	0,35972	41,032	109,877
Step at 7195'			
09/02/2011 10:57	0,36806	41,087	110,315
09/02/2011 10:57	0,37639	41,157	110,681
09/02/2011 10:58	0,38472	41,221	111,163
09/02/2011 10:58	0,39306	41,269	111,486
Step at 7245'			
09/02/2011 10:59	0,40139	41,304	111,714
09/02/2011 10:59	0,40972	44,65	112,143
09/02/2011 11:00	0,41806	44,52	114,2
09/02/2011 11:00	0,42639	42,758	115,506
Step at 7295'			
09/02/2011 11:01	0,43472	42,618	116,169
09/02/2011 11:01	0,44306	58,537	116,688
09/02/2011 11:02	0,45139	58,486	116,909
09/02/2011 11:02	0,45972	58,431	116,968
Step at 7345'			
09/02/2011 11:03	0,46806	59,823	116,984
09/02/2011 11:03	0,47639	73,383	117,069
09/02/2011 11:04	0,48472	73,361	117,084
09/02/2011 11:04	0,49306	73,317	117,071
Step at 7395'			
09/02/2011 11:05	0,50139	80,231	117,063
09/02/2011 11:05	0,50972	88,192	117,016
09/02/2011 11:06	0,51806	88,17	116,977
09/02/2011 11:06	0,52639	88,119	116,952
Step at 7445'			
09/02/2011 11:07	0,53472	93,369	116,934
09/02/2011 11:07	0,54306	95,663	116,834
09/02/2011 11:08	0,55139	95,627	116,775
09/02/2011 11:08	0,55972	95,558	116,743
Step at 7495'			
09/02/2011 11:09	0,56806	99,672	116,709
09/02/2011 11:09	0,57639	99,634	116,626
09/02/2011 11:10	0,58472	99,574	116,595
09/02/2011 11:10	0,59306	99,492	116,567
Step at 7515'			
09/02/2011 11:11	0,60139	105,381	116,499
09/02/2011 11:11	0,60972	105,352	116,454
09/02/2011 11:12	0,61806	105,321	116,438
09/02/2011 11:12	0,62639	111,313	116,414
Step at 7535'			
09/02/2011 11:13	0,63472	111,304	116,361
09/02/2011 11:13	0,64306	111,268	116,343
Step at 7555'			
09/02/2011 11:14	0,65139	111,213	116,336
09/02/2011 11:14	0,65972	117,882	116,549
09/02/2011 11:15	0,66806	117,857	116,839
09/02/2011 11:15	0,67639	117,841	116,96
Step at 7575'			
09/02/2011 11:16	0,68472	120,31	117,092
09/02/2011 11:16	0,69306	120,296	117,365
09/02/2011 11:17	0,70139	120,303	117,465
09/02/2011 11:17	0,70972	120,309	117,631

Well:	LO16-7 Development Test		
Memory Gauge:	SN 2760 with Battery PPS 8060C		
Time	Elapsed Time	Pressure	Temperature
(Real - Time)	(Hours)	(Psia)	(DegF)
Step at 7595', log for 3 Hrs. With gas lift			
09/02/2011 11:18	0,71806	120,365	117,759
09/02/2011 11:18	0,72639	120,449	117,811
09/02/2011 11:19	0,73472	120,591	117,825
09/02/2011 11:19	0,74306	120,775	117,821
09/02/2011 11:20	0,75139	120,987	117,811
09/02/2011 11:20	0,75972	121,193	117,812
09/02/2011 11:21	0,76806	121,327	117,798
09/02/2011 11:21	0,77639	121,32	117,806
09/02/2011 11:22	0,78472	121,129	117,8
09/02/2011 11:22	0,79306	120,827	117,781
09/02/2011 11:23	0,80139	120,417	117,786
09/02/2011 11:23	0,80972	119,975	117,802
09/02/2011 11:24	0,81806	119,563	117,816
09/02/2011 11:24	0,82639	119,26	117,832
09/02/2011 11:25	0,83472	119,03	117,846
09/02/2011 11:25	0,84306	118,838	117,859
09/02/2011 11:26	0,85139	118,71	117,882
09/02/2011 11:26	0,85972	118,603	117,899
09/02/2011 11:27	0,86806	118,385	117,93
09/02/2011 11:27	0,87639	118,26	117,935
09/02/2011 11:28	0,88472	118,186	117,937
09/02/2011 11:28	0,89306	118,232	117,957
09/02/2011 11:29	0,90139	118,342	117,971
09/02/2011 11:29	0,90972	118,62	117,977
09/02/2011 11:30	0,91806	118,852	117,974
09/02/2011 11:30	0,92639	119,064	117,976
09/02/2011 11:31	0,93472	119,203	117,978
09/02/2011 11:31	0,94306	119,335	117,974
09/02/2011 11:32	0,95139	119,411	117,972
09/02/2011 11:32	0,95972	119,396	117,977
09/02/2011 11:33	0,96806	119,337	117,996
09/02/2011 11:33	0,97639	119,161	118,009
09/02/2011 11:34	0,98472	118,973	118,022
09/02/2011 11:34	0,99306	118,762	118,036
09/02/2011 11:35	1,00139	118,585	118,045
09/02/2011 11:35	1,00972	118,467	118,049
09/02/2011 11:36	1,01806	118,428	118,062
09/02/2011 11:36	1,02639	118,393	118,069
09/02/2011 11:37	1,03472	118,377	118,077
09/02/2011 11:37	1,04306	118,428	118,088
09/02/2011 11:38	1,05139	118,441	118,1
09/02/2011 11:38	1,05972	118,463	118,111
09/02/2011 11:39	1,06806	118,514	118,109
09/02/2011 11:39	1,07639	118,6	118,122
09/02/2011 11:40	1,08472	118,692	118,119
09/02/2011 11:40	1,09306	118,867	118,12
09/02/2011 11:41	1,10139	119,113	118,123
09/02/2011 11:41	1,10972	119,346	118,114
09/02/2011 11:42	1,11806	119,632	118,114
09/02/2011 11:42	1,12639	119,935	118,108
09/02/2011 11:43	1,13472	120,195	118,103
09/02/2011 11:43	1,14306	120,347	118,097
09/02/2011 11:44	1,15139	120,459	118,098
09/02/2011 11:44	1,15972	120,545	118,083
09/02/2011 11:45	1,16806	120,645	118,08
09/02/2011 11:45	1,17639	120,763	118,077
09/02/2011 11:46	1,18472	120,937	118,079
09/02/2011 11:46	1,19306	121,141	118,074
09/02/2011 11:47	1,20139	121,345	118,078
09/02/2011 11:47	1,20972	121,53	118,074
09/02/2011 11:48	1,21806	121,692	118,07
09/02/2011 11:48	1,22639	121,867	118,062
09/02/2011 11:49	1,23472	122,088	118,058
09/02/2011 11:49	1,24306	122,293	118,051

Well:	LO16-7 Development Test		
Memory Gauge:	SN 2760 with Battery PPS 8060C		
Time	Elapsed Time	Pressure	Temperature
(Real - Time)	(Hours)	(Psia)	(DegF)
09/02/2011 11:50	1,25139	122,458	118,038
09/02/2011 11:50	1,25972	122,695	118,036
09/02/2011 11:51	1,26806	122,88	118,024
09/02/2011 11:51	1,27639	123,044	118,018
09/02/2011 11:52	1,28472	123,235	118,015
09/02/2011 11:52	1,29306	123,427	118,011
09/02/2011 11:53	1,30139	123,538	118,002
09/02/2011 11:53	1,30972	123,714	117,997
09/02/2011 11:54	1,31806	123,884	117,991
09/02/2011 11:54	1,32639	123,997	117,987
09/02/2011 11:55	1,33472	124,065	117,979
09/02/2011 11:55	1,34306	124,124	117,972
09/02/2011 11:56	1,35139	124,111	117,962
09/02/2011 11:56	1,35972	124,039	117,959
09/02/2011 11:57	1,36806	123,945	117,951
09/02/2011 11:57	1,37639	123,835	117,944
09/02/2011 11:58	1,38472	123,715	117,936
09/02/2011 11:58	1,39306	123,603	117,925
09/02/2011 11:59	1,40139	188,752	117,966
09/02/2011 11:59	1,40972	242,915	117,958
09/02/2011 12:00	1,41806	282,887	117,892
09/02/2011 12:00	1,42639	314,806	117,815
09/02/2011 12:01	1,43472	344,584	117,744
09/02/2011 12:01	1,44306	369,178	117,707
09/02/2011 12:02	1,45139	390,277	117,686
09/02/2011 12:02	1,45972	408,686	117,677
09/02/2011 12:03	1,46806	423,897	117,663
09/02/2011 12:03	1,47639	435,835	117,65
09/02/2011 12:04	1,48472	445,577	117,627
09/02/2011 12:04	1,49306	453,566	117,6
09/02/2011 12:05	1,50139	445,077	117,563
09/02/2011 12:05	1,50972	424,474	117,52
09/02/2011 12:06	1,51806	403,38	117,477
09/02/2011 12:06	1,52639	379,797	117,419
09/02/2011 12:07	1,53472	353,578	117,363
09/02/2011 12:07	1,54306	325,464	117,301
09/02/2011 12:08	1,55139	295,829	117,23
09/02/2011 12:08	1,55972	265,036	117,159
09/02/2011 12:09	1,56806	234,442	117,086
09/02/2011 12:09	1,57639	204,749	117,006
09/02/2011 12:10	1,58472	177,526	116,917
09/02/2011 12:10	1,59306	154,955	116,823
09/02/2011 12:11	1,60139	135,627	116,736
09/02/2011 12:11	1,60972	123,836	116,641
09/02/2011 12:12	1,61806	121,226	116,308
09/02/2011 12:12	1,62639	118,955	116,021
09/02/2011 12:13	1,63472	116,445	115,952
09/02/2011 12:13	1,64306	116,402	116,05
09/02/2011 12:14	1,65139	116,202	116,137
09/02/2011 12:14	1,65972	115,83	116,224
09/02/2011 12:15	1,66806	115,401	116,32
09/02/2011 12:15	1,67639	114,927	116,427
09/02/2011 12:16	1,68472	114,486	116,535
09/02/2011 12:16	1,69306	114,181	116,646
09/02/2011 12:17	1,70139	114,041	116,739
09/02/2011 12:17	1,70972	113,951	116,826
09/02/2011 12:18	1,71806	113,94	116,885
09/02/2011 12:18	1,72639	113,942	116,93
09/02/2011 12:19	1,73472	113,98	116,956
09/02/2011 12:19	1,74306	114,148	116,98
09/02/2011 12:20	1,75139	114,421	116,988
09/02/2011 12:20	1,75972	114,655	116,992
09/02/2011 12:21	1,76806	116,272	117,02
09/02/2011 12:21	1,77639	116,321	117,023
09/02/2011 12:22	1,78472	116,347	117,026

Well: LO16-7 Development Test			
Memory Gauge: SN 2760 with Battery PPS 8060C			
Time	Elapsed Time	Pressure	Temperature
(Real - Time)	(Hours)	(Psia)	(DegF)
09/02/2011 12:22	1,79306	116,403	117,035
09/02/2011 12:23	1,80139	116,543	117,045
09/02/2011 12:23	1,80972	116,773	117,057
09/02/2011 12:24	1,81806	117,028	117,073
09/02/2011 12:24	1,82639	117,398	117,086
09/02/2011 12:25	1,83472	119,464	117,107
09/02/2011 12:25	1,84306	120,502	117,124
09/02/2011 12:26	1,85139	120,534	117,149
09/02/2011 12:26	1,85972	121,747	117,169
09/02/2011 12:27	1,86806	121,945	117,196
09/02/2011 12:27	1,87639	122,31	117,217
09/02/2011 12:28	1,88472	122,82	117,237
09/02/2011 12:28	1,89306	123,456	117,258
09/02/2011 12:29	1,90139	124,287	117,277
09/02/2011 12:29	1,90972	125,069	117,293
09/02/2011 12:30	1,91806	125,836	117,308
09/02/2011 12:30	1,92639	126,606	117,315
09/02/2011 12:31	1,93472	127,424	117,327
09/02/2011 12:31	1,94306	128,158	117,34
09/02/2011 12:32	1,95139	128,88	117,351
09/02/2011 12:32	1,95972	129,554	117,36
09/02/2011 12:33	1,96806	130,167	117,376
09/02/2011 12:33	1,97639	130,712	117,384
09/02/2011 12:34	1,98472	131,222	117,392
09/02/2011 12:34	1,99306	131,672	117,407
09/02/2011 12:35	2,00139	132,081	117,425
09/02/2011 12:35	2,00972	132,555	117,434
09/02/2011 12:36	2,01806	133,038	117,45
09/02/2011 12:36	2,02639	133,516	117,464
09/02/2011 12:37	2,03472	133,983	117,474
09/02/2011 12:37	2,04306	134,459	117,481
09/02/2011 12:38	2,05139	134,774	117,488
09/02/2011 12:38	2,05972	134,975	117,494
09/02/2011 12:39	2,06806	135,138	117,51
09/02/2011 12:39	2,07639	135,262	117,516
09/02/2011 12:40	2,08472	135,423	117,527
09/02/2011 12:40	2,09306	135,664	117,538
09/02/2011 12:41	2,10139	135,979	117,544
09/02/2011 12:41	2,10972	136,369	117,555
09/02/2011 12:42	2,11806	136,819	117,569
09/02/2011 12:42	2,12639	137,261	117,586
09/02/2011 12:43	2,13472	137,689	117,602
09/02/2011 12:43	2,14306	138,024	117,612
09/02/2011 12:44	2,15139	138,301	117,631
09/02/2011 12:44	2,15972	138,596	117,643
09/02/2011 12:45	2,16806	138,89	117,662
09/02/2011 12:45	2,17639	139,22	117,676
09/02/2011 12:46	2,18472	139,677	117,689
09/02/2011 12:46	2,19306	140,164	117,695
09/02/2011 12:47	2,20139	140,648	117,7
09/02/2011 12:47	2,20972	141,098	117,711
09/02/2011 12:48	2,21806	141,511	117,719
09/02/2011 12:48	2,22639	141,881	117,718
09/02/2011 12:49	2,23472	142,238	117,725
09/02/2011 12:49	2,24306	142,545	117,727
09/02/2011 12:50	2,25139	142,837	117,733
09/02/2011 12:50	2,25972	143,109	117,735
09/02/2011 12:51	2,26806	143,377	117,737
09/02/2011 12:51	2,27639	143,597	117,739
09/02/2011 12:52	2,28472	143,809	117,743
09/02/2011 12:52	2,29306	144,03	117,737
09/02/2011 12:53	2,30139	144,251	117,742
09/02/2011 12:53	2,30972	144,447	117,738
09/02/2011 12:54	2,31806	144,663	117,74
09/02/2011 12:54	2,32639	144,866	117,744

Well: LO16-7 Development Test			
Memory Gauge: SN 2760 with Battery PPS 8060C			
Time	Elapsed Time	Pressure	Temperature
(Real - Time)	(Hours)	(Psia)	(DegF)
09/02/2011 12:55	2,33472	145,053	117,74
09/02/2011 12:55	2,34306	145,248	117,738
09/02/2011 12:56	2,35139	145,423	117,74
09/02/2011 12:56	2,35972	145,584	117,729
09/02/2011 12:57	2,36806	145,769	117,719
09/02/2011 12:57	2,37639	145,929	117,708
09/02/2011 12:58	2,38472	146,068	117,697
09/02/2011 12:58	2,39306	166,868	117,678
09/02/2011 12:59	2,40139	218,003	117,777
09/02/2011 12:59	2,40972	272,617	117,816
09/02/2011 13:00	2,41806	314,274	117,843
09/02/2011 13:00	2,42639	347,685	117,858
09/02/2011 13:01	2,43472	379,423	117,866
09/02/2011 13:01	2,44306	408,766	117,869
09/02/2011 13:02	2,45139	434,005	117,864
09/02/2011 13:02	2,45972	453,538	117,868
09/02/2011 13:03	2,46806	469,366	117,855
09/02/2011 13:03	2,47639	481,745	117,844
09/02/2011 13:04	2,48472	492,369	117,831
09/02/2011 13:04	2,49306	501,428	117,809
09/02/2011 13:05	2,50139	492,285	117,789
09/02/2011 13:05	2,50972	466,834	117,754
09/02/2011 13:06	2,51806	438,236	117,719
09/02/2011 13:06	2,52639	406,844	117,68
09/02/2011 13:07	2,53472	373,908	117,631
09/02/2011 13:07	2,54306	340,682	117,587
09/02/2011 13:08	2,55139	307,368	117,534
09/02/2011 13:08	2,55972	273,671	117,474
09/02/2011 13:09	2,56806	240,853	117,418
09/02/2011 13:09	2,57639	209,691	117,357
09/02/2011 13:10	2,58472	182,28	117,3
09/02/2011 13:10	2,59306	159,424	117,235
09/02/2011 13:11	2,60139	140,005	117,178
09/02/2011 13:11	2,60972	123,427	117,125
09/02/2011 13:12	2,61806	118,445	116,888
09/02/2011 13:12	2,62639	116,165	116,627
09/02/2011 13:13	2,63472	114,777	116,518
09/02/2011 13:13	2,64306	113,318	116,513
09/02/2011 13:14	2,65139	112,089	116,597
09/02/2011 13:14	2,65972	111,066	116,718
09/02/2011 13:15	2,66806	110,919	116,869
09/02/2011 13:15	2,67639	110,743	117,016
09/02/2011 13:16	2,68472	110,626	117,178
09/02/2011 13:16	2,69306	110,549	117,349
09/02/2011 13:17	2,70139	110,489	117,519
09/02/2011 13:17	2,70972	110,661	117,677
09/02/2011 13:18	2,71806	110,996	117,791
09/02/2011 13:18	2,72639	111,43	117,788
09/02/2011 13:19	2,73472	112,012	117,747
09/02/2011 13:19	2,74306	114,833	117,706
09/02/2011 13:20	2,75139	116,049	117,68
09/02/2011 13:20	2,75972	116,241	117,668
09/02/2011 13:21	2,76806	118,152	117,639
09/02/2011 13:21	2,77639	118,31	117,597
09/02/2011 13:22	2,78472	118,594	117,562
09/02/2011 13:22	2,79306	118,989	117,535
09/02/2011 13:23	2,80139	119,48	117,508
09/02/2011 13:23	2,80972	120,053	117,489
09/02/2011 13:24	2,81806	120,554	117,476
09/02/2011 13:24	2,82639	120,99	117,464
09/02/2011 13:25	2,83472	121,447	117,459
09/02/2011 13:25	2,84306	123,578	117,453
09/02/2011 13:26	2,85139	124,691	117,443
09/02/2011 13:26	2,85972	124,751	117,427
09/02/2011 13:27	2,86806	124,946	117,414

Well: LO16-7 Development Test			
Memory Gauge: SN 2760 with Battery PPS 8060C			
Time	Elapsed Time	Pressure	Temperature
(Real - Time)	(Hours)	(Psia)	(DegF)
09/02/2011 13:27	2,87639	125,273	117,398
09/02/2011 13:28	2,88472	125,722	117,391
09/02/2011 13:28	2,89306	126,279	117,4
09/02/2011 13:29	2,90139	126,892	117,413
09/02/2011 13:29	2,90972	127,513	117,426
09/02/2011 13:30	2,91806	128,125	117,443
09/02/2011 13:30	2,92639	128,734	117,462
09/02/2011 13:31	2,93472	129,347	117,481
09/02/2011 13:31	2,94306	129,953	117,508
09/02/2011 13:32	2,95139	130,521	117,518
09/02/2011 13:32	2,95972	131,067	117,487
09/02/2011 13:33	2,96806	131,597	117,471
09/02/2011 13:33	2,97639	132,101	117,467
09/02/2011 13:34	2,98472	132,506	117,457
09/02/2011 13:34	2,99306	132,833	117,465
09/02/2011 13:35	3,00139	133,122	117,478
09/02/2011 13:35	3,00972	133,332	117,492
09/02/2011 13:36	3,01806	133,445	117,517
09/02/2011 13:36	3,02639	133,574	117,542
09/02/2011 13:37	3,03472	133,708	117,553
09/02/2011 13:37	3,04306	133,8	117,551
09/02/2011 13:38	3,05139	133,877	117,552
09/02/2011 13:38	3,05972	133,995	117,547
09/02/2011 13:39	3,06806	134,194	117,548
09/02/2011 13:39	3,07639	134,469	117,554
09/02/2011 13:40	3,08472	134,842	117,566
09/02/2011 13:40	3,09306	135,3	117,572
09/02/2011 13:41	3,10139	135,821	117,583
09/02/2011 13:41	3,10972	136,329	117,594
09/02/2011 13:42	3,11806	136,842	117,602
09/02/2011 13:42	3,12639	137,335	117,612
09/02/2011 13:43	3,13472	137,761	117,624
09/02/2011 13:43	3,14306	138,048	117,636
09/02/2011 13:44	3,15139	138,297	117,646
09/02/2011 13:44	3,15972	138,526	117,654
09/02/2011 13:45	3,16806	138,758	117,672
09/02/2011 13:45	3,17639	139,054	117,675
09/02/2011 13:46	3,18472	139,464	117,686
09/02/2011 13:46	3,19306	139,872	117,699
09/02/2011 13:47	3,20139	140,236	117,708
09/02/2011 13:47	3,20972	140,568	117,716
09/02/2011 13:48	3,21806	140,861	117,723
09/02/2011 13:48	3,22639	141,111	117,732
09/02/2011 13:49	3,23472	141,38	117,74
09/02/2011 13:49	3,24306	141,641	117,746
09/02/2011 13:50	3,25139	141,884	117,757
09/02/2011 13:50	3,25972	142,117	117,763
09/02/2011 13:51	3,26806	142,366	117,771
09/02/2011 13:51	3,27639	142,58	117,775
09/02/2011 13:52	3,28472	142,78	117,783
09/02/2011 13:52	3,29306	142,986	117,789
09/02/2011 13:53	3,30139	143,191	117,793
09/02/2011 13:53	3,30972	143,386	117,792
09/02/2011 13:54	3,31806	143,585	117,796
09/02/2011 13:54	3,32639	143,801	117,799
09/02/2011 13:55	3,33472	143,982	117,807
09/02/2011 13:55	3,34306	144,164	117,803
09/02/2011 13:56	3,35139	144,344	117,81
09/02/2011 13:56	3,35972	144,522	117,821
09/02/2011 13:57	3,36806	144,7	117,818
09/02/2011 13:57	3,37639	144,884	117,823
09/02/2011 13:58	3,38472	145,054	117,827
09/02/2011 13:58	3,39306	161,704	117,827
09/02/2011 13:59	3,40139	217,409	117,862
09/02/2011 13:59	3,40972	271,541	117,879

Well: LO16-7 Development Test			
Memory Gauge: SN 2760 with Battery PPS 8060C			
Time	Elapsed Time	Pressure	Temperature
(Real - Time)	(Hours)	(Psia)	(DegF)
09/02/2011 14:00	3,41806	312,7	117,9
09/02/2011 14:00	3,42639	345,554	117,91
09/02/2011 14:01	3,43472	376,959	117,935
09/02/2011 14:01	3,44306	405,345	117,949
09/02/2011 14:02	3,45139	428,475	117,963
09/02/2011 14:02	3,45972	445,909	117,974
09/02/2011 14:03	3,46806	460,727	117,981
09/02/2011 14:03	3,47639	473,345	117,99
09/02/2011 14:04	3,48472	484,71	117,99
09/02/2011 14:04	3,49306	493,212	117,989
09/02/2011 14:05	3,50139	481,249	117,969
09/02/2011 14:05	3,50972	454,616	117,947
09/02/2011 14:06	3,51806	425,997	117,926
09/02/2011 14:06	3,52639	395,442	117,885
09/02/2011 14:07	3,53472	363,627	117,84
09/02/2011 14:07	3,54306	331,534	117,797
09/02/2011 14:08	3,55139	299,354	117,745
09/02/2011 14:08	3,55972	266,872	117,689
09/02/2011 14:09	3,56806	234,975	117,632
09/02/2011 14:09	3,57639	204,989	117,566
09/02/2011 14:10	3,58472	178,316	117,505
09/02/2011 14:10	3,59306	156,235	117,447
09/02/2011 14:11	3,60139	137,368	117,384
09/02/2011 14:11	3,60972	121,456	117,323
09/02/2011 14:12	3,61806	118,456	116,99
09/02/2011 14:12	3,62639	116,148	116,587
09/02/2011 14:13	3,63472	114,487	116,416
09/02/2011 14:13	3,64306	112,956	116,402
09/02/2011 14:14	3,65139	112,819	116,492
09/02/2011 14:14	3,65972	112,626	116,658
09/02/2011 14:15	3,66806	112,416	116,859
09/02/2011 14:15	3,67639	112,169	117,068
09/02/2011 14:16	3,68472	111,957	117,265
09/02/2011 14:16	3,69306	111,937	117,411
09/02/2011 14:17	3,70139	112,047	117,528
09/02/2011 14:17	3,70972	112,252	117,596
09/02/2011 14:18	3,71806	112,57	117,602
09/02/2011 14:18	3,72639	112,838	117,59
09/02/2011 14:19	3,73472	113,116	117,593
09/02/2011 14:19	3,74306	114,604	117,606
09/02/2011 14:20	3,75139	114,732	117,611
09/02/2011 14:20	3,75972	115,032	117,604
09/02/2011 14:21	3,76806	115,482	117,586
09/02/2011 14:21	3,77639	116,039	117,564
09/02/2011 14:22	3,78472	116,67	117,537
09/02/2011 14:22	3,79306	117,267	117,509
09/02/2011 14:23	3,80139	117,753	117,476
09/02/2011 14:23	3,80972	118,14	117,44
09/02/2011 14:24	3,81806	118,455	117,412
09/02/2011 14:24	3,82639	118,803	117,381
09/02/2011 14:25	3,83472	120,543	117,358
Cut off gas lift and production valve, log for 2 hrs.			
09/02/2011 14:25	3,84306	120,736	117,335
09/02/2011 14:26	3,85139	121,084	117,309
09/02/2011 14:26	3,85972	121,57	117,284
09/02/2011 14:27	3,86806	122,161	117,259
09/02/2011 14:27	3,87639	122,865	117,245
09/02/2011 14:28	3,88472	123,457	117,227
09/02/2011 14:28	3,89306	124,022	117,226
09/02/2011 14:29	3,90139	124,587	117,216
09/02/2011 14:29	3,90972	125,19	117,224
09/02/2011 14:30	3,91806	125,78	117,229
09/02/2011 14:30	3,92639	126,407	117,233
09/02/2011 14:31	3,93472	126,998	117,236
09/02/2011 14:31	3,94306	127,557	117,247

Well: LO16-7 Development Test			
Memory Gauge: SN 2760 with Battery PPS 8060C			
Time	Elapsed Time	Pressure	Temperature
(Real - Time)	(Hours)	(Psia)	(DegF)
09/02/2011 14:32	3,95139	128,063	117,263
09/02/2011 14:32	3,95972	128,589	117,291
09/02/2011 14:33	3,96806	129,073	117,325
09/02/2011 14:33	3,97639	129,568	117,353
09/02/2011 14:34	3,98472	130,059	117,387
09/02/2011 14:34	3,99306	130,539	117,417
09/02/2011 14:35	4,00139	130,985	117,454
09/02/2011 14:35	4,00972	131,425	117,486
09/02/2011 14:36	4,01806	131,835	117,524
09/02/2011 14:36	4,02639	132,226	117,559
09/02/2011 14:37	4,03472	132,605	117,59
09/02/2011 14:37	4,04306	132,97	117,632
09/02/2011 14:38	4,05139	133,313	117,663
09/02/2011 14:38	4,05972	133,661	117,696
09/02/2011 14:39	4,06806	133,989	117,731
09/02/2011 14:39	4,07639	134,321	117,754
09/02/2011 14:40	4,08472	134,651	117,752
09/02/2011 14:40	4,09306	134,984	117,744
09/02/2011 14:41	4,10139	135,297	117,744
09/02/2011 14:41	4,10972	135,605	117,734
09/02/2011 14:42	4,11806	135,894	117,74
09/02/2011 14:42	4,12639	136,174	117,732
09/02/2011 14:43	4,13472	136,447	117,732
09/02/2011 14:43	4,14306	136,706	117,729
09/02/2011 14:44	4,15139	136,98	117,725
09/02/2011 14:44	4,15972	137,244	117,726
09/02/2011 14:45	4,16806	137,492	117,73
09/02/2011 14:45	4,17639	137,727	117,733
09/02/2011 14:46	4,18472	137,974	117,731
09/02/2011 14:46	4,19306	138,198	117,733
09/02/2011 14:47	4,20139	138,432	117,738
09/02/2011 14:47	4,20972	138,657	117,74
09/02/2011 14:48	4,21806	138,897	117,742
09/02/2011 14:48	4,22639	139,132	117,746
09/02/2011 14:49	4,23472	139,344	117,752
09/02/2011 14:49	4,24306	139,528	117,753
09/02/2011 14:50	4,25139	139,723	117,761
09/02/2011 14:50	4,25972	139,899	117,76
09/02/2011 14:51	4,26806	140,072	117,766
09/02/2011 14:51	4,27639	140,24	117,769
09/02/2011 14:52	4,28472	140,408	117,769
09/02/2011 14:52	4,29306	140,578	117,768
09/02/2011 14:53	4,30139	140,745	117,77
09/02/2011 14:53	4,30972	140,9	117,768
09/02/2011 14:54	4,31806	141,06	117,769
09/02/2011 14:54	4,32639	141,215	117,766
09/02/2011 14:55	4,33472	141,355	117,767
09/02/2011 14:55	4,34306	141,5	117,762
09/02/2011 14:56	4,35139	141,633	117,766
09/02/2011 14:56	4,35972	141,766	117,77
09/02/2011 14:57	4,36806	141,904	117,77
09/02/2011 14:57	4,37639	142,03	117,774
09/02/2011 14:58	4,38472	142,152	117,772
09/02/2011 14:58	4,39306	142,267	117,773
09/02/2011 14:59	4,40139	142,372	117,78
09/02/2011 14:59	4,40972	142,478	117,787
09/02/2011 15:00	4,41806	142,57	117,795
09/02/2011 15:00	4,42639	142,672	117,799
09/02/2011 15:01	4,43472	142,766	117,806
09/02/2011 15:01	4,44306	142,858	117,81
09/02/2011 15:02	4,45139	142,935	117,822
09/02/2011 15:02	4,45972	143,044	117,824
09/02/2011 15:03	4,46806	143,129	117,83
09/02/2011 15:03	4,47639	143,208	117,838
09/02/2011 15:04	4,48472	143,281	117,85

Well: LO16-7 Development Test			
Memory Gauge: SN 2760 with Battery PPS 8060C			
Time	Elapsed Time	Pressure	Temperature
(Real - Time)	(Hours)	(Psia)	(DegF)
09/02/2011 15:04	4,49306	143,37	117,861
09/02/2011 15:05	4,50139	143,43	117,88
09/02/2011 15:05	4,50972	143,482	117,892
09/02/2011 15:06	4,51806	143,544	117,908
09/02/2011 15:06	4,52639	143,6	117,923
09/02/2011 15:07	4,53472	143,648	117,937
09/02/2011 15:07	4,54306	143,698	117,952
09/02/2011 15:08	4,55139	143,755	117,965
09/02/2011 15:08	4,55972	143,823	117,98
09/02/2011 15:09	4,56806	143,89	117,999
09/02/2011 15:09	4,57639	143,958	118,014
09/02/2011 15:10	4,58472	144,031	118,032
09/02/2011 15:10	4,59306	144,087	118,049
09/02/2011 15:11	4,60139	144,138	118,062
09/02/2011 15:11	4,60972	144,192	118,077
09/02/2011 15:12	4,61806	144,229	118,091
09/02/2011 15:12	4,62639	144,26	118,104
09/02/2011 15:13	4,63472	144,314	118,113
09/02/2011 15:13	4,64306	144,359	118,125
09/02/2011 15:14	4,65139	144,394	118,137
09/02/2011 15:14	4,65972	144,449	118,145
09/02/2011 15:15	4,66806	144,482	118,157
09/02/2011 15:15	4,67639	144,527	118,166
09/02/2011 15:16	4,68472	144,574	118,174
09/02/2011 15:16	4,69306	144,638	118,18
09/02/2011 15:17	4,70139	144,693	118,181
09/02/2011 15:17	4,70972	144,767	118,19
09/02/2011 15:18	4,71806	144,818	118,194
09/02/2011 15:18	4,72639	144,859	118,2
09/02/2011 15:19	4,73472	144,903	118,204
09/02/2011 15:19	4,74306	144,942	118,207
09/02/2011 15:20	4,75139	144,976	118,211
09/02/2011 15:20	4,75972	145,015	118,207
09/02/2011 15:21	4,76806	145,059	118,217
09/02/2011 15:21	4,77639	145,098	118,214
09/02/2011 15:22	4,78472	145,142	118,215
09/02/2011 15:22	4,79306	145,197	118,212
09/02/2011 15:23	4,80139	145,244	118,211
09/02/2011 15:23	4,80972	145,29	118,207
09/02/2011 15:24	4,81806	145,32	118,205
09/02/2011 15:24	4,82639	145,352	118,202
09/02/2011 15:25	4,83472	145,373	118,19
09/02/2011 15:25	4,84306	145,398	118,189
09/02/2011 15:26	4,85139	145,432	118,183
09/02/2011 15:26	4,85972	145,478	118,17
09/02/2011 15:27	4,86806	145,507	118,17
09/02/2011 15:27	4,87639	145,539	118,16
09/02/2011 15:28	4,88472	145,579	118,16
09/02/2011 15:28	4,89306	145,616	118,158
09/02/2011 15:29	4,90139	145,652	118,157
09/02/2011 15:29	4,90972	145,691	118,159
09/02/2011 15:30	4,91806	145,724	118,157
09/02/2011 15:30	4,92639	145,76	118,155
09/02/2011 15:31	4,93472	145,787	118,156
09/02/2011 15:31	4,94306	145,812	118,155
09/02/2011 15:32	4,95139	145,84	118,157
09/02/2011 15:32	4,95972	145,875	118,154
09/02/2011 15:33	4,96806	145,898	118,148
09/02/2011 15:33	4,97639	145,921	118,152
09/02/2011 15:34	4,98472	145,937	118,145
09/02/2011 15:34	4,99306	145,952	118,149
09/02/2011 15:35	5,00139	145,992	118,147
09/02/2011 15:35	5,00972	146,018	118,146
09/02/2011 15:36	5,01806	146,058	118,143
09/02/2011 15:36	5,02639	146,095	118,149

Well: LO16-7 Development Test			
Memory Gauge: SN 2760 with Battery PPS 8060C			
Time	Elapsed Time	Pressure	Temperature
(Real - Time)	(Hours)	(Psia)	(DegF)
09/02/2011 15:37	5,03472	146,132	118,146
09/02/2011 15:37	5,04306	146,154	118,143
09/02/2011 15:38	5,05139	146,174	118,145
09/02/2011 15:38	5,05972	146,202	118,145
09/02/2011 15:39	5,06806	146,231	118,146
09/02/2011 15:39	5,07639	146,257	118,146
09/02/2011 15:40	5,08472	146,275	118,149
09/02/2011 15:40	5,09306	146,312	118,151
09/02/2011 15:41	5,10139	146,337	118,149
09/02/2011 15:41	5,10972	146,368	118,152
09/02/2011 15:42	5,11806	146,397	118,15
09/02/2011 15:42	5,12639	146,422	118,153
09/02/2011 15:43	5,13472	146,446	118,154
09/02/2011 15:43	5,14306	146,465	118,157
09/02/2011 15:44	5,15139	146,481	118,156
09/02/2011 15:44	5,15972	146,512	118,158
09/02/2011 15:45	5,16806	146,525	118,153
09/02/2011 15:45	5,17639	146,563	118,161
09/02/2011 15:46	5,18472	146,597	118,162
09/02/2011 15:46	5,19306	146,615	118,163
09/02/2011 15:47	5,20139	146,638	118,161
09/02/2011 15:47	5,20972	146,669	118,161
09/02/2011 15:48	5,21806	146,683	118,163
09/02/2011 15:48	5,22639	146,691	118,167
09/02/2011 15:49	5,23472	146,714	118,17
09/02/2011 15:49	5,24306	146,735	118,169
09/02/2011 15:50	5,25139	146,767	118,169
09/02/2011 15:50	5,25972	146,777	118,17
09/02/2011 15:51	5,26806	146,804	118,17
09/02/2011 15:51	5,27639	146,821	118,173
09/02/2011 15:52	5,28472	146,843	118,175
09/02/2011 15:52	5,29306	146,857	118,175
09/02/2011 15:53	5,30139	146,873	118,177
09/02/2011 15:53	5,30972	146,89	118,177
09/02/2011 15:54	5,31806	146,922	118,18
09/02/2011 15:54	5,32639	146,939	118,182
09/02/2011 15:55	5,33472	146,963	118,18
09/02/2011 15:55	5,34306	146,986	118,183
09/02/2011 15:56	5,35139	147,008	118,187
09/02/2011 15:56	5,35972	147,027	118,19
09/02/2011 15:57	5,36806	147,049	118,185
09/02/2011 15:57	5,37639	147,05	118,187
09/02/2011 15:58	5,38472	147,076	118,199
09/02/2011 15:58	5,39306	147,093	118,191
09/02/2011 15:59	5,40139	147,103	118,193
09/02/2011 15:59	5,40972	147,119	118,194
09/02/2011 16:00	5,41806	147,151	118,197
09/02/2011 16:00	5,42639	147,162	118,202
09/02/2011 16:01	5,43472	147,181	118,206
09/02/2011 16:01	5,44306	147,209	118,202
09/02/2011 16:02	5,45139	147,222	118,209
09/02/2011 16:02	5,45972	147,25	118,213
09/02/2011 16:03	5,46806	147,273	118,209
09/02/2011 16:03	5,47639	147,292	118,216
09/02/2011 16:04	5,48472	147,291	118,215
09/02/2011 16:04	5,49306	147,309	118,218
09/02/2011 16:05	5,50139	147,331	118,222
09/02/2011 16:05	5,50972	147,358	118,225
09/02/2011 16:06	5,51806	147,379	118,235
09/02/2011 16:06	5,52639	147,406	118,234
09/02/2011 16:07	5,53472	147,421	118,234
09/02/2011 16:07	5,54306	147,43	118,24
09/02/2011 16:08	5,55139	147,441	118,244
09/02/2011 16:08	5,55972	147,45	118,246
09/02/2011 16:09	5,56806	147,469	118,248

Well: LO16-7 Development Test			
Memory Gauge: SN 2760 with Battery PPS 8060C			
Time	Elapsed Time	Pressure	Temperature
(Real - Time)	(Hours)	(Psia)	(DegF)
09/02/2011 16:09	5,57639	147,468	118,259
09/02/2011 16:10	5,58472	147,479	118,258
09/02/2011 16:10	5,59306	147,502	118,26
09/02/2011 16:11	5,60139	147,512	118,266
09/02/2011 16:11	5,60972	147,531	118,27
09/02/2011 16:12	5,61806	147,561	118,272
09/02/2011 16:12	5,62639	147,585	118,274
09/02/2011 16:13	5,63472	147,593	118,28
09/02/2011 16:13	5,64306	147,616	118,288
09/02/2011 16:14	5,65139	147,64	118,285
09/02/2011 16:14	5,65972	147,674	118,291
09/02/2011 16:15	5,66806	147,682	118,291
09/02/2011 16:15	5,67639	147,697	118,299
09/02/2011 16:16	5,68472	147,717	118,296
09/02/2011 16:16	5,69306	147,713	118,306
09/02/2011 16:17	5,70139	147,709	118,307
09/02/2011 16:17	5,70972	147,731	118,308
09/02/2011 16:18	5,71806	147,747	118,311
09/02/2011 16:18	5,72639	147,754	118,314
09/02/2011 16:19	5,73472	147,776	118,311
09/02/2011 16:19	5,74306	147,806	118,317
09/02/2011 16:20	5,75139	147,808	118,321
09/02/2011 16:20	5,75972	147,82	118,319
09/02/2011 16:21	5,76806	145,397	118,289
09/02/2011 16:21	5,77639	145,4	118,248
09/02/2011 16:22	5,78472	145,412	118,229
09/02/2011 16:22	5,79306	138,551	118,208
09/02/2011 16:23	5,80139	129,542	117,858
09/02/2011 16:23	5,80972	129,541	117,776
POOH Memory Gauges, Step at 7595'			
09/02/2011 16:24	5,81806	129,557	117,752
09/02/2011 16:24	5,82639	129,563	117,733
09/02/2011 16:25	5,83472	114,66	117,659
09/02/2011 16:25	5,84306	114,625	117,618
Step at 7545'			
09/02/2011 16:26	5,85139	114,594	117,621
09/02/2011 16:26	5,85972	114,566	117,621
09/02/2011 16:27	5,86806	112,908	117,624
09/02/2011 16:27	5,87639	98,915	117,673
09/02/2011 16:28	5,88472	98,901	117,694
09/02/2011 16:28	5,89306	98,905	117,701
Step at 7495'			
09/02/2011 16:29	5,90139	98,898	117,709
09/02/2011 16:29	5,90972	83,287	117,736
09/02/2011 16:30	5,91806	83,267	117,785
09/02/2011 16:30	5,92639	83,247	117,796
Step at 7445'			
09/02/2011 16:31	5,93472	83,234	117,803
09/02/2011 16:31	5,94306	83,226	117,802
09/02/2011 16:32	5,95139	68,152	117,814
09/02/2011 16:32	5,95972	68,064	117,9
Step at 7395'			
09/02/2011 16:33	5,96806	67,974	117,922
09/02/2011 16:33	5,97639	67,902	117,936
09/02/2011 16:34	5,98472	67,818	117,94
09/02/2011 16:34	5,99306	52,436	117,978
09/02/2011 16:35	6,00139	52,436	118,016
09/02/2011 16:35	6,00972	52,429	118,022
Step at 7345'			
09/02/2011 16:36	6,01806	52,427	118,027
09/02/2011 16:36	6,02639	41,407	118,025
09/02/2011 16:37	6,03472	41,404	118,014
09/02/2011 16:37	6,04306	41,417	118,002
Step at 7295'			
09/02/2011 16:38	6,05139	41,423	117,993

Well:	LO16-7 Development Test		
Memory Gauge:	SN 2760 with Battery PPS 8060C		
Time	Elapsed Time	Pressure	Temperature
(Real - Time)	(Hours)	(Psia)	(DegF)
09/02/2011 16:38	6,05972	41,414	117,991
09/02/2011 16:39	6,06806	41,411	117,983
09/02/2011 16:39	6,07639	41,414	117,974
Step at 7245'			
09/02/2011 16:40	6,08472	41,399	117,974
09/02/2011 16:40	6,09306	41,382	117,97
09/02/2011 16:41	6,10139	41,374	117,961
09/02/2011 16:41	6,10972	41,367	117,955
Step at 7195'			
09/02/2011 16:42	6,11806	41,354	117,952
09/02/2011 16:42	6,12639	41,332	117,949
09/02/2011 16:43	6,13472	41,335	117,94
09/02/2011 16:43	6,14306	41,317	117,931
09/02/2011 16:44	6,15139	41,308	117,929
09/02/2011 16:44	6,15972	41,285	117,928
Step at 7145'			
09/02/2011 16:45	6,16806	41,267	117,92
09/02/2011 16:45	6,17639	41,25	117,919
09/02/2011 16:46	6,18472	41,24	117,929
09/02/2011 16:46	6,19306	41,219	117,93
Step at 7095'			
09/02/2011 16:47	6,20139	41,233	117,946
09/02/2011 16:47	6,20972	41,238	117,947
09/02/2011 16:48	6,21806	41,199	117,973
09/02/2011 16:48	6,22639	41,181	117,991
Step at 7045'			
09/02/2011 16:49	6,23472	41,171	117,998
09/02/2011 16:49	6,24306	41,138	118,006
09/02/2011 16:50	6,25139	41,088	118,023
09/02/2011 16:50	6,25972	41,068	118,034
Step at 6945'			
09/02/2011 16:51	6,26806	41,066	118,034
09/02/2011 16:51	6,27639	41,048	118,038
09/02/2011 16:52	6,28472	41,026	118,036
09/02/2011 16:52	6,29306	41,018	118,039
09/02/2011 16:53	6,30139	41,012	118,038
09/02/2011 16:53	6,30972	40,972	118,038
Step at 6845'			
09/02/2011 16:54	6,31806	40,954	118,031
09/02/2011 16:54	6,32639	40,925	118,027
09/02/2011 16:55	6,33472	40,912	118,007
09/02/2011 16:55	6,34306	40,905	117,993
Step at 6745'			
09/02/2011 16:56	6,35139	40,904	117,98
09/02/2011 16:56	6,35972	40,862	117,967
09/02/2011 16:57	6,36806	40,802	117,952
09/02/2011 16:57	6,37639	40,68	117,815
Step at 6645'			
09/02/2011 16:58	6,38472	40,453	117,429
09/02/2011 16:58	6,39306	40,134	116,725
09/02/2011 16:59	6,40139	39,74	115,802
09/02/2011 16:59	6,40972	39,281	114,677
09/02/2011 17:00	6,41806	38,748	113,296
09/02/2011 17:00	6,42639	38,174	111,629
09/02/2011 17:01	6,43472	37,58	109,61
09/02/2011 17:01	6,44306	36,921	107,296
09/02/2011 17:02	6,45139	36,204	104,701
09/02/2011 17:02	6,45972	35,507	102,026
09/02/2011 17:03	6,46806	34,853	99,72
09/02/2011 17:03	6,47639	34,206	97,24
09/02/2011 17:04	6,48472	33,612	94,651
09/02/2011 17:04	6,49306	33,083	92,549
09/02/2011 17:05	6,50139	32,595	90,683
09/02/2011 17:05	6,50972	32,152	88,888
09/02/2011 17:06	6,51806	31,778	87,933

Well:	LO16-7 Development Test		
Memory Gauge:	SN 2760 with Battery PPS 8060C		
Time	Elapsed Time	Pressure	Temperature
(Real - Time)	(Hours)	(Psia)	(DegF)
09/02/2011 17:06	6,52639	31,505	87,927
09/02/2011 17:07	6,53472	31,327	88,079
09/02/2011 17:07	6,54306	31,21	88,233
09/02/2011 17:08	6,55139	31,143	88,378
09/02/2011 17:08	6,55972	31,093	88,517
09/02/2011 17:09	6,56806	15,579	88,602
09/02/2011 17:09	6,57639	15,578	88,69
Step at 0'			
09/02/2011 17:10	6,58472	15,576	88,79
09/02/2011 17:10	6,59306	15,573	88,871
09/02/2011 17:11	6,60139	15,573	88,479

Desactive M.G.
